

## Progress Summary





95%

Seapen

80%

Growing Tanks

80%

Hatchery Tanks

## Table of Content



Seapen with a knock-down wooden gazebo

#### **II** Growing tanks


4

III Hatchery Tank Rack

#### 10 IV Future Plan



## I. Seapen with a knock-down wooden gazebo

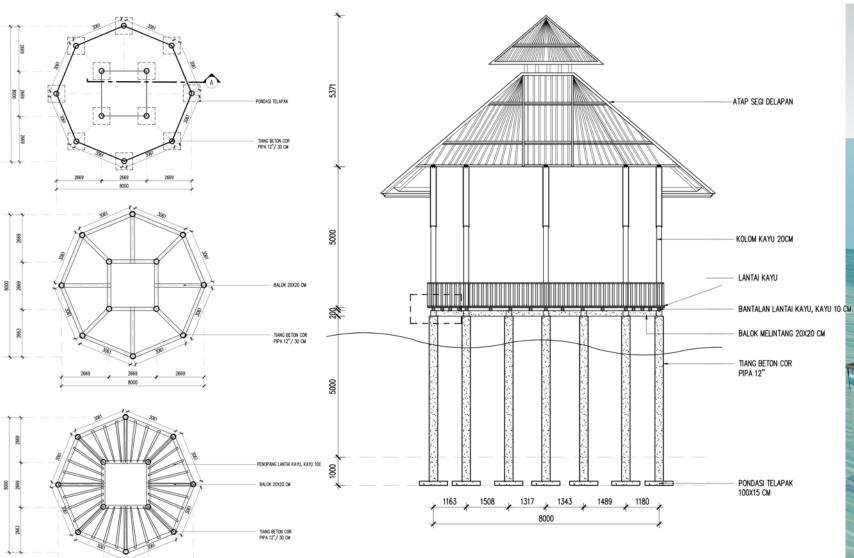





### **PROGRESS DESCRIPTION**


### Dec 31<sup>th</sup> , 2021

- 1. The thatch roof is set,
- 2. The floating platform attached to the building,
- 3. Tidying up the site,
- 4. Purchased the solar panel electricity set,
- Purchased the net and will be set up nearly when the pups are ready to move

#### The final progress is 95%

#### The works left are

- Setting up the electricity, Solar Panel Set, and lights,
- Installation of netting around footers (postponed until just prior to first delivery of eggs)

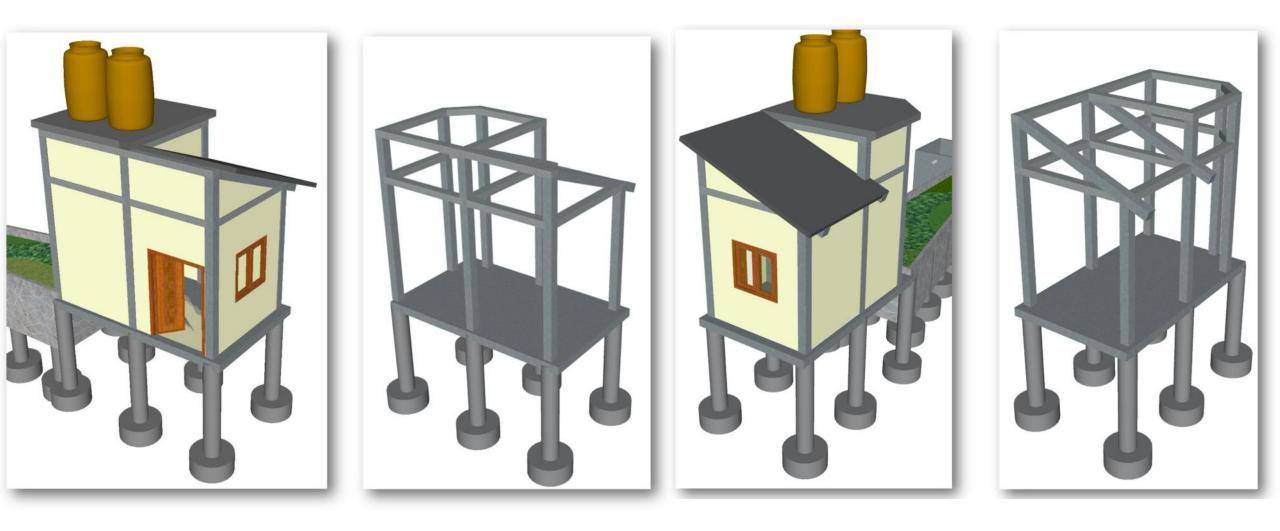



### PROGRESS DESCRIPTION

### Dec 31<sup>th</sup> , 2021

- 1. The room is finished,
- 2. The doors and windows are finished,
- 3. The painting is finished,
- 4. Purchased 1 unit 3000 liters of water tank, &
- 5. Cleaned the area.

#### The final progress is 80%

#### The works left are

- 1. Confirm reservoir tanks with husbandry group, and
- Awaiting further details on life support system from husbandry group.

## III. Hatchery Tank Rack





### PROGRESS DESCRIPTION

### Dec 31<sup>th</sup> , 2021

- 1. Planned the woods,
- 2. Varnished the woods,
- 3. Set the structure,
- Team has assembled all the plank woods, wooden structure in the Site, and
- 5. Signboard plank wood

#### The final progress is 80%

#### The works left are

 Awaiting further details on life support system from husbandry group.

## Future Plan

## Seapen

- Installation of glass panels in floor (awaiting delivery of panels, estimated to arrive on November 25<sup>th</sup>, 2022)
- Installation of netting around footers (postponed until just prior to first delivery of eggs)

# Growing Tanks

- 1. confirm reservoir tanks with husbandry group, and
- Awaiting further details on life support system from husbandry group.

# Hatchery Tanks

 awaiting further details on life support system from husbandry group

